

\\cse01\g\3493\Plans\06 Maintenance of Traffic\mda_detour.dwg | Layout1 | 9/15/2008 2:46 AM |

SEQUENCE OF OPERATIONS

Phase I

- Construct temporary widening along north side of West 3rd Street as shown.
- Shift traffic to the westbound lanes.
- Construct the proposed eastbound lanes as shown.
- Construct additional temporary widening along the south side of West 3rd Street as shown.

Phase II


- Shift traffic to the newly constructed eastbound lanes.
- Construct the proposed median and westbound lanes.
- Shift traffic to final configuration.
- Close the outermost eastbound lane and construct the final portions of curb and sidewalk.

Phase III

- West 3rd Street shall be closed to thru traffic at the direction of the Engineer. Closure shall be limited to one week, unless directed by the engineer, for construction of the railroad crossing. Traffic shall be directed as shown on this sheet during the closure.

NOTE:

Short term closure of West 3rd Street for replacement of railroad crossing only. West 3rd Street to remain open at all other times. Detour to be removed upon completion of railroad crossing or as directed by the Engineer.

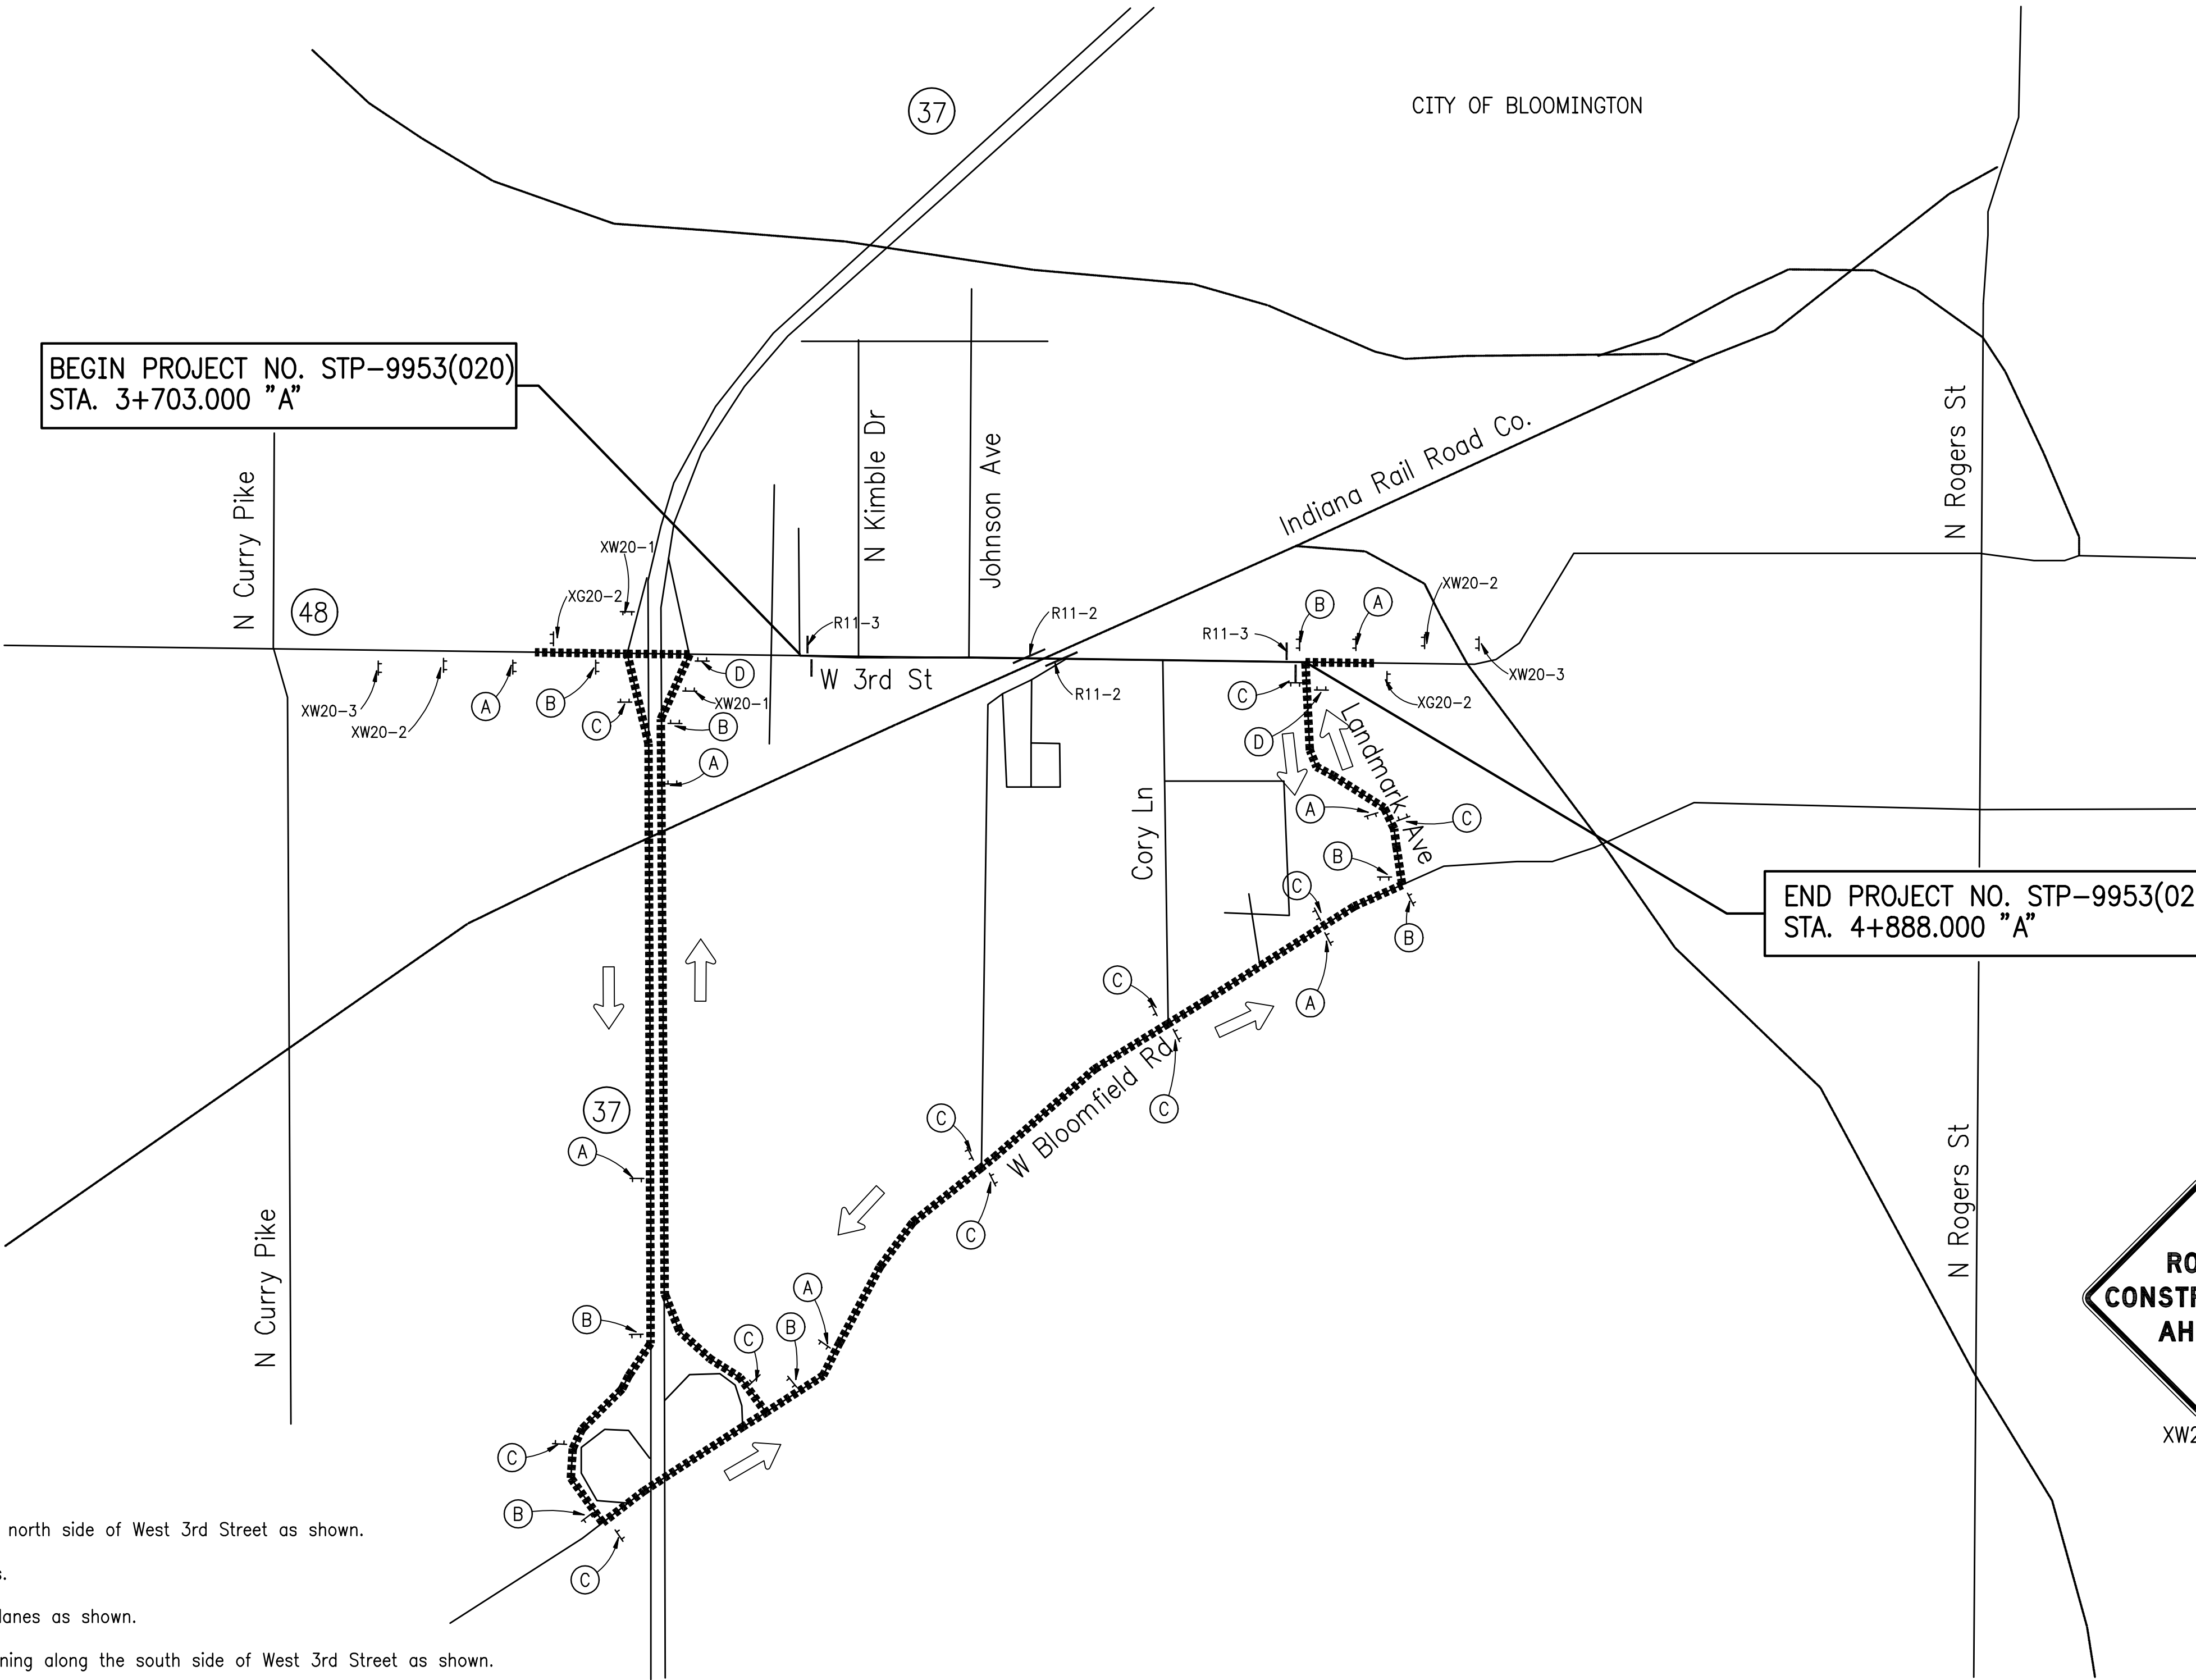

LEGEND

- Type III-A Barricades
- - - Type III-B Barricades

**ROAD
CLOSED**

R11-2

**ROAD CLOSED AHEAD
LOCAL TRAFFIC ONLY**

R11-3



XW20-1



WX20-2




XW20-3

**END
CONSTRUCTION**


XG20-2

Detour Route Marker Assemblies

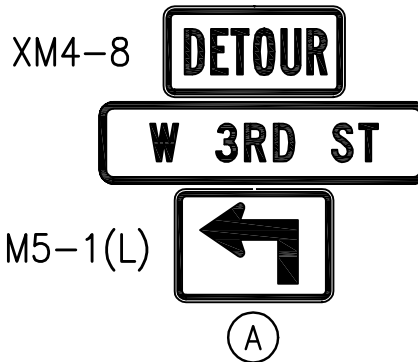


M5-1(L)

(A)

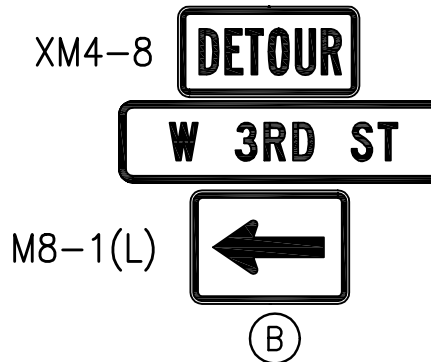


M8-1(L)

(B)

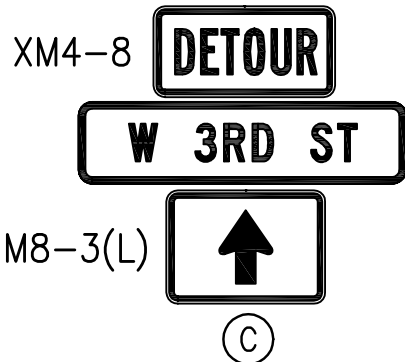

M8-3(L)

(C)

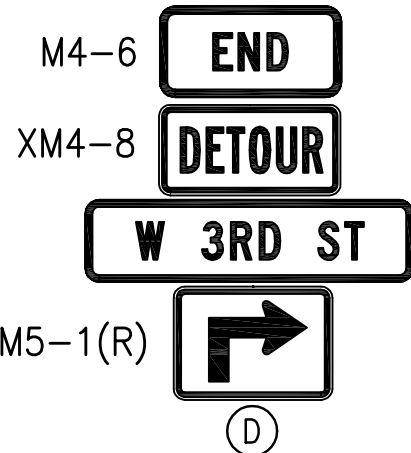

M5-1(R)

(D)

CITY OF BLOOMINGTON

MAINTENANCE OF TRAFFIC
DETOUR MAP

RECOMMENDED
FOR APPROVAL _____
DESIGN ENGINEER DATE

DESIGNED: KLV DRAWN: EAM

CHECKED: DJG CHECKED: DJG

HORIZONTAL SCALE	BRIDGE FILE
1:1000	
VERTICAL SCALE	DESIGNATION NO.
N.A.	0300766

SURVEY BOOK	SHEETS
	5 of
CONTRACT	PROJECT NO.
R-30350	STP-9953(020)
